Project Title :RESIDENTIAL BUILDING











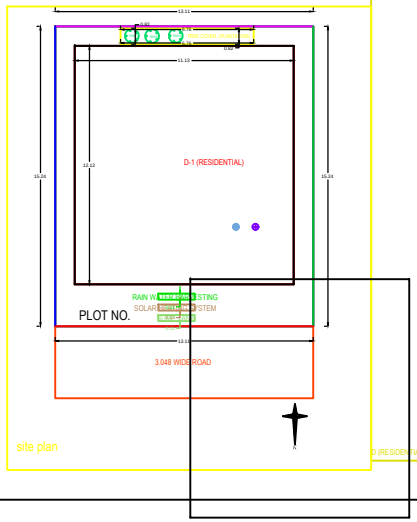

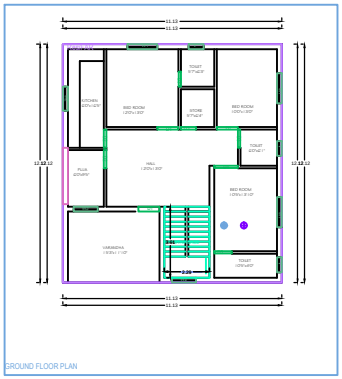

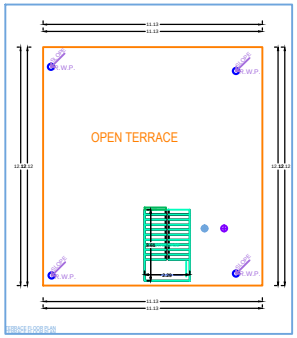





AREA STATEMENT: RAMGARH NAGAR PARISHAD		VERSION NO.: 1.0.37
		VERSION DATE: 16/10/2020
PROJECT DETAIL:		-
Invard_No : -		Plot Use : Residential
Region : JHARKHAND URBAN LOCAL BODIES		Plot SubUse : Residential Bldg(Apartment)
District : RAMGARH		Land Use Zone : NA
Application Type : General Proposal		Abutting Road Width : -
Project Type : Building Permission		Plot No. : -
Nature of Development : New		Revenue Survey No/Survey No. : -
Location : Old Area		Thana No : -
Sub Location : NA		Holding No : -
Village/Mauza Name : -		Khata No : -
Ward No : -		North : -
Road/Street : -		South : -
		East : -
		West : -

AREA DETAILS:		SQ.MT.
AREA OF PLOT (Minimum)	(A)	199.74
Net Plot Area (Gross Plot Area - Deduction from Gross Plot area)	(A-Deductions)	199.74
Deductions for Balance Plot Area (from 'Gross Plot Area)		
COP Area		5.55
Total		5.55
Balance Plot Area (Net Plot Area - Recreational/Amenity space)	(A-Deductions)	194.19
Plot Area for Coverage (Net Plot Area)	(A-Deductions)	199.74
Plot Area for FSI (Net Plot Area + Road Widening Area)	(A-Deductions)	199.74
COVERAGE CHECK		
Proposed Coverage Area (67.49 %)		134.79
Total Coverage Area (67.49 %)		134.79
FAR CHECK		
Proposed Area of FAR		134.79
Total Area of FAR		134.79
BUILT UP AREA CHECK		
Total Proposed BuiltUp Area		134.79
ARCH / ENGR / SUPERVISOR (Regd)		OWNER
DEVELOPMENT AUTHORITY		LOCAL BODY

COLOR INDEX

PLOT BOUNDARY	
ABUTTING ROAD	
PROPOSED WORK (COVERAGE AREA)	
EXISTING (To be retained)	
EXISTING (To be demolished)	

Color Index:

MARGIN DETAIL:

Building / Wing Name	Road Name	Front Margin	Rear Margin	Side1 Margin	Side2 Margin
D-1 (RESIDENTIAL)	3.048 WIDE ROAD	2.13	0.99	0.99	0.99

FAR & Tenement Details (Table 4c-1)

Building	No. of Same Bldg.	Total Built Up Area (Sq.mt.)	Proposed FAR Area (Sq.mt.) Resi.	Total FAR Area (Sq.mt.)	Tnmt (No.)
D (RESIDENTIAL)	1	134.79	134.79	134.79	01
Grand Total:	1	134.79	134.79	134.79	01

Building :D (RESIDENTIAL)

Floor Name	Total Built Up Area (Sq.mt.)	Proposed FAR Area (Sq.mt.)		Total FAR Area (Sq.mt.)	Tnmt (No.)
		Resi.			
Ground Floor	134.79	134.79		134.79	01
Terrace Floor	0.00	0.00		0.00	00
Total:	134.79	134.79		134.79	01
Total Number of Same Buildings	1				
Total:	134.79	134.79		134.79	01

SCHEDULE OF JOINERY:

BUILDING NAME	NAME	LENGTH	HEIGHT	NOS
D (RESIDENTIAL)	D3	0.76	2.10	02
D (RESIDENTIAL)	D3	0.89	2.10	01
D (RESIDENTIAL)	D2	0.91	2.10	01
D (RESIDENTIAL)	D2	0.91	2.10	02
D (RESIDENTIAL)	D1	1.07	2.10	03
D (RESIDENTIAL)	D1	1.09	2.10	01
D (RESIDENTIAL)	D1	1.19	2.10	01
Total:	-	-	-	11

SCHEDULE OF JOINERY:

BUILDING NAME	NAME	LENGTH	HEIGHT	NOS
D (RESIDENTIAL)	V	0.76	1.00	03
D (RESIDENTIAL)	W2	1.22	1.50	02
D (RESIDENTIAL)	W3	1.22	1.50	01
D (RESIDENTIAL)	W1	1.52	1.50	03
Total:	-	-	-	09

UnitBUA Table for Building :D (RESIDENTIAL)

FLOOR	Name	UnitBUA Type	UnitBUA Area	Carpet Area	No. of Rooms	No. of Tenement
GROUND FLOOR PLAN	Resi/FAR	FLAT	134.79	134.06	11	1
Total:	-	-	134.79	134.06	11	1
